



RAIGANJ MUNICIPALITY

CONSTRUCTION SITE FIRST VISIT REPORT

First Visit : PROP-00036 - Shaktinagar Graveyard

Location Details

Name of the Location	Latitude & Longitude	Ward	Area	Area Unit
Shaktinagar Graveyard	22.579729 88.4135567	8	Shaktinagar Graveyard	Acre

Project Details

Proposed Project Type	Toilet Seat (Male)	Toilet Seat (Female)	Urinal Seat (Male)	Urinal Seat (Female)
PT (Public Toilet Project)	4	4	4	4

Land Details

Classification	Plot No.	Jl No.	Dag No.	Khatian No.	Mouza	Possession Details (Owned by)
Other	4447	151	4447	1090, 3692	Mohanbati	

Foundation upto Tie beam with reinforcement details

Visit Date	22/12/2025						
Earth Cutting (1200 x 1200 x 1000)	Column Nos.	Length (M)	Breath (M)	Height (M)	Status	Remarks	
	10	1200	1200	1000	OK	OK	

Earth Cutting Image



Re-inforcement

Footing
(10 mm dia 10 nos both)

Rod Nos.	Diameter (M)	Status	Remarks
10	10	OK	OK

Footing Image



Column
(12 mm dia 6 nos)

Rod Nos.	Diameter (M)	Length (M)	Height (M)	Status	Remarks
6	12	250	250	OK	OK


Column Image



Tie beam
(12 mm dia 4 nos)

Rod Nos.	Diameter (M)	Length (M)	Breath (M)	Status	Remarks
4	12	250	250	OK	OK

Tie beam Image

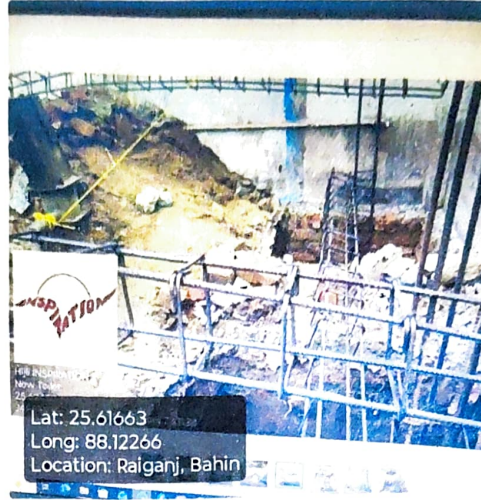

Binder for Column 8 mm dia 175 mm C/C

Status

Remarks

OK

OK

Binder for Tie 8 mm dia 175 mm C/C

Status

Remarks

OK

OK

Overall Remarks

Ok

Overall Work Status - Images

Photo 1 - Angle 1


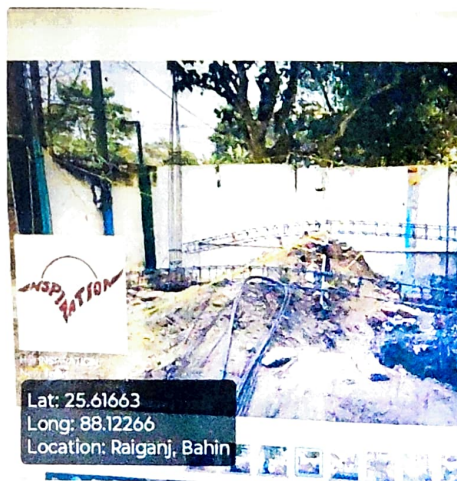



Photo 2 - Angle 2



QR Code Board Image

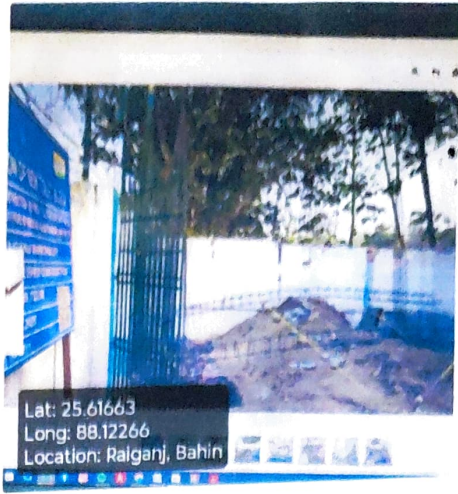

Signature of Engineer


Seal with signature of ULB Engineer
Name : _____
Contact no. : _____

Sub-Assistant Engineer
Raiganj Municipality
Uttar Dinajpur

Signature of Engineer
HILLI INSPIRATION
Name : _____
Contact no. : _____


Co-ordinator
Hilli INSPIRATION
