



RAIGANJ MUNICIPALITY

CONSTRUCTION SITE FIRST VISIT REPORT

First Visit : PROP-00620 - Madina Jame Masjid

Location Details

Name of the Location	Latitude & Longitude	Ward	Area	Area Unit
Madina Jame Masjid	22.579731 88.4135381	15	Paschim Birnagar	Acre

Project Details

Proposed Project Type	Toilet Seat (Male)	Toilet Seat (Female)	Urinal Seat (Male)	Urinal Seat (Female)
PT (Public Toilet Project)	7	4	7	4

Land Details

Classification	Plot No.	Jl No.	Dag No.	Khatian No.	Mouza	Possession Details (Owned by)
Other	662, 663	150	662, 663	386	Raiganj	

Foundation upto Tie beam with reinforcement details


Visit Date

22/12/2025

Earth Cutting
(1200 x 1200 x 1000)

Column Nos.	Length (M)	Breath (M)	Height (M)	Status	Remarks
10	1200	1200	1000	OK	OK

Earth Cutting Image

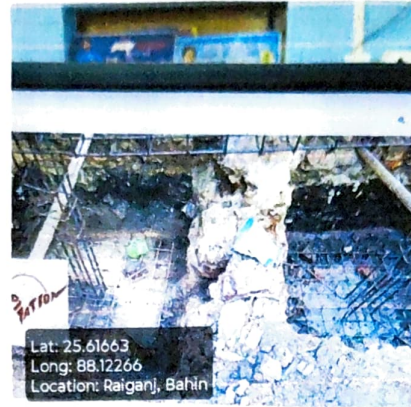

Re-inforcement

Footing
(10 mm dia 10 nos both)

Rod Nos.	Diameter (M)	Status	Remarks
10	10	OK	OK


Footing Image



Column
(12 mm dia 6 nos)

Rod Nos.	Diameter (M)	Length (M)	Height (M)	Status	Remarks
6	12	250	250	OK	OK

Column Image

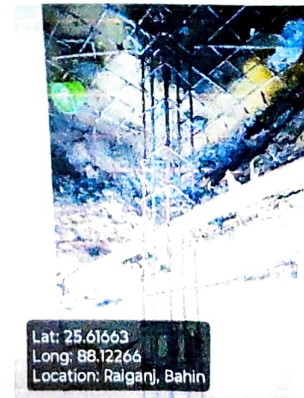

Tie beam
(12 mm dia 4 nos)

Rod Nos.	Diameter (M)	Length (M)	Breath (M)	Status	Remarks
4	12	250	250	OK	OK

Tie beam Image

Photo 1 - Angle 1



Photo 2 - Angle 2



QR Code Board Image



Signatures & Approval

Seal with signature of ULB Engineer

Name : _____

Contact no. : _____

Sub-Assistant Engineer
Raiganj Municipality
Uttar Dinajpur

Signature of Engineer

HILLI INSPIRATION

Name : _____

Contact no. : _____

M. D. D.
Co-ordinator
HILLI INSPIRATION
