RANAGHAT MUNICIPALITY

CONSTRUCTION SITE FIRST VISIT REPORT

First Visit : PROP-01264 - COURTMORE

Location Details

Name of the Location	Latitude & Longitude	Ward	Area	Area Unit
COURTMORE	22.5796839 88.4135298	10	009	Acre

Project Details

Proposed Project Type	Toilet Seat (Male)	Toilet Seat (Female)	Urinal Seat (Male)	Urinal Seat (Female)
PT (Public Toilet Project)	2	2	3	2

Land Details

Classification	Plot No.	JI No.	Dag No.	Khatian No.	Mouza	Possession Details (Owned by)
Danga	46	155	46	8647	RANAGHAT I	

Foundation upto Tie beam with reinforcement details

Visit Date: 08/12/2025

Earth Cutting (1200 x 1200 x 1000)	Column Nos.	Length (M)	Breath (M)	Height (M)	Status	Remarks
	10	1200	1200	1000	OK	OK

Earth Cutting Image

Re-inforcement

Footing (10 mm dia 10 nos both)	Rod Nos.	Diameter (M)	Status	Remarks
	10	10	OK	OK

Footing Image

Column (12 mm dia 6 nos)	Rod Nos.	Diameter (M)	Length (M)	Height (M)	Status	Remarks
	6	12	250	250	OK	OK

Column Image

Tie beam (12 mm dia 4 nos)	Rod Nos.	Diameter (M)	Length (M)	Breath (M)	Status	Remarks
	4	12	250	250	OK	OK

Tie beam Image

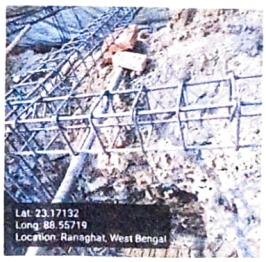

Binder for Column 8 mm dia 175 mm C/C	Status	Remarks
	OK	OK

Binder for Tie 6 mm dia 175 mm C/C	Status	Remarks
	OK	OK

Overall Reamrks: OK

Photo 1 - Angle 1

Overall Work Status - Images

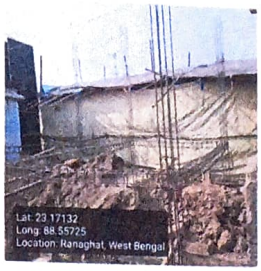

Photo 2 - Angle 2

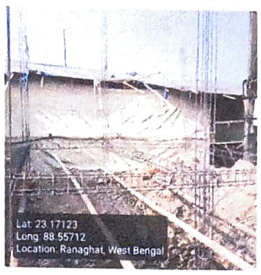

QR Code Board Image

Signatures & Approval

30/12/25

Seal with signature of ULB Engineer
Name:
Contact no.:

Sub Assistant Engineer
Ranaghat Municipality

Suprimo Ghosh 30/12/25

Signature of Engineer
HILLI INSPIRATION
Name : SUPRIMO GHOSH
Contact no. : 8622075848

Checked & Verified

Engineer (Civil)
Hijli INSPIRATION

30/12/25

Signature of Co-Ordinator
HILLI INSPIRATION

Co-ordinator
Hijli INSPIRATION
